


Longmeadow Parkway

February 2019

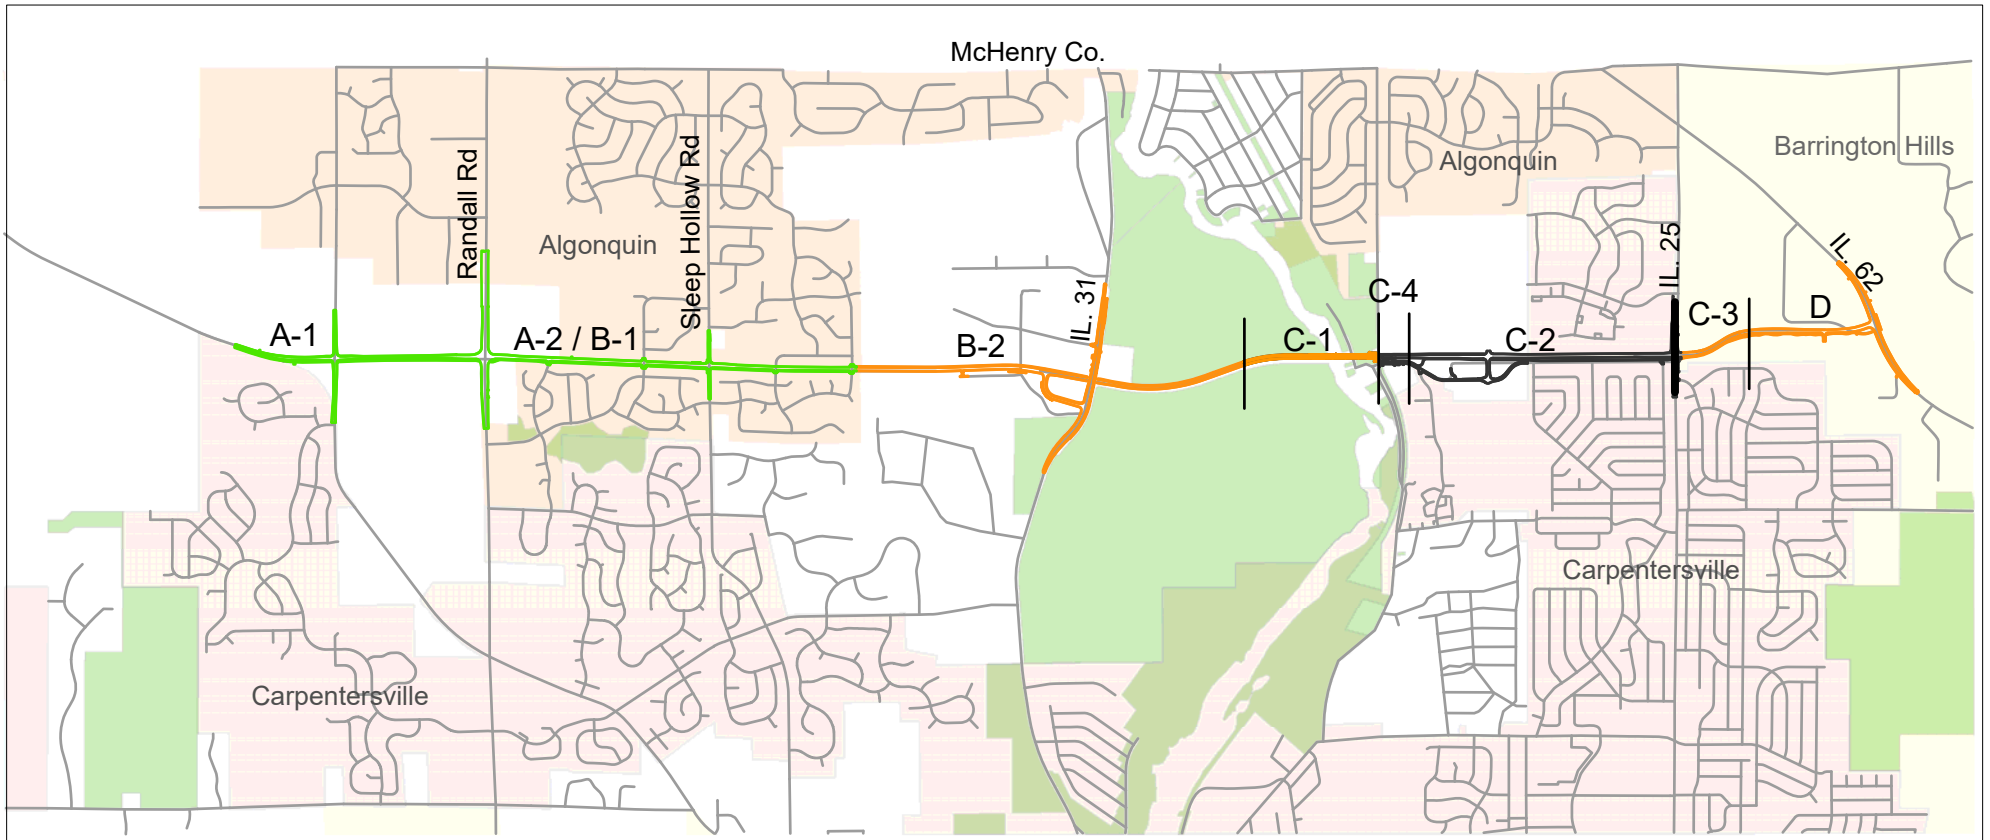

Status:

A-1, A-2/B-1 are complete

B-2 Construction from January 2018 to October 2019

D Construction from January 2018 to June 2019




C-1 Construction of new bridge over Fox River from January 2019 to November 2020

C-2 Pursuing remaining land acquisition. Anticipated construction January 2020 to August 2021

C-3 Construction from January 2019 to November 2019

C-4 Toll Collection Facility anticipated construction January 2021 to December 2021

Legend

-  Construction Complete
-  Under Construction
-  Targeting Construction Early 2019-2021
